



PUBLIC WORKS DEPARTMENT

Project: **Borgfeld Dr Phase II**

Precinct: 3


Location / Limits:

From Timberline Dr to FM 2696 (Blanco Rd) including Old Blanco Rd south of Borgfeld Drive.

Scope:

The project consists of 2 miles of roadway reconstruction to two-12 ft. travel lanes in each direction designated turn lanes at intersections, two 4-foot shoulders and necessary drainage.

Status: Construction (75 %)

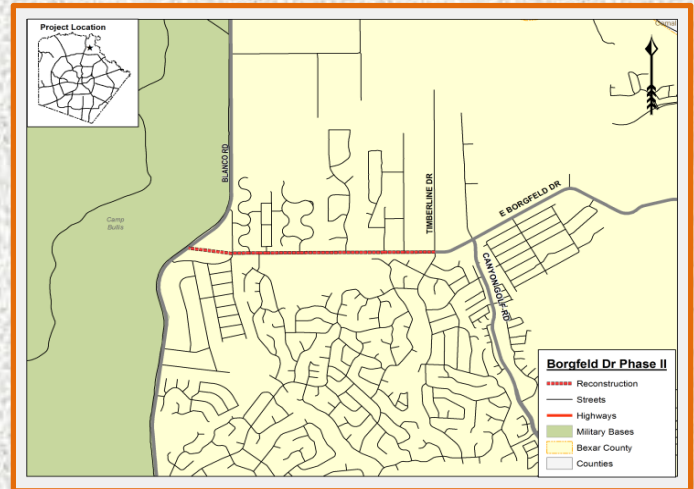

Additional Information:

Consultant: CDS Muery Services

Contractor: Texas Sterling

Construction Cost: \$ 8, 356,223.99

Joint Bid: SAWS Water & CPS Gas

Advertise Date: January 6, 2017

Construction Start Date: March 20, 2017

Construction End Date: 1 Q 2019



PUBLIC WORKS DEPARTMENT

Project: **Bulverde Rd Phase IV**

Precinct: 3


Location / Limits:

Expansion of Bulverde Rd from Marshall Road to approximately 6,300 ft. north.

Scope:

Project will expand the existing two lane rural roadway section to an urban roadway section consisting of two 12 foot travel lanes in each direction with a 14 foot center median/turn lane within an 86' ROW (Typical).

Status: Final Design /Utility Relocation

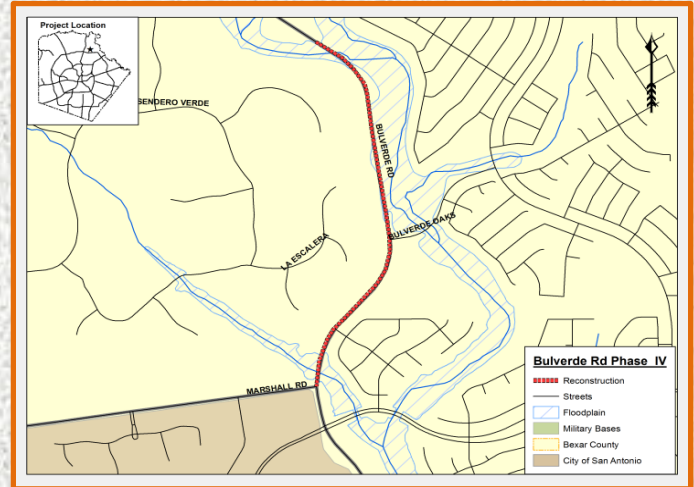

Additional Information:

Consultant: LAN Inc.

Contractor: TBD

Construction Cost: \$ 7,631,293

Joint Bid: SAWS , CPS Gas

Advertise Date: 3 Q 2018

Construction Start Date: 4 Q 2018

Construction End Date: 2 Q 2020

MPO Project



PUBLIC WORKS DEPARTMENT

Project: **Marshall Rd**


Precinct: 3

Location / Limits:

From US 281 expressway overpass to Bulverde Rd.

Scope:

Roadway widening approximately 4700 LF of Marshall Rd from its existing two-lane section to a typical section that will provide operational improvements, added capacity or a combination of the two, with necessary drainage improvements, and anticipated bicycle/pedestrian amenities.

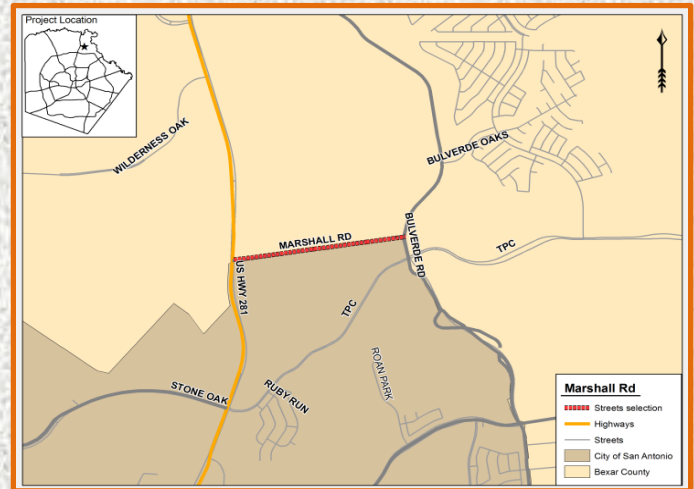

Status: Bidding Phase

Additional Information:

Consultant: Poznecki-Camarillo

Contractor: TBD

Construction Cost: \$ 4,228,770

Joint Bid: SAWS

Advertise Date: May 18, 2018

Construction Start Date: 4 Q 2018

Construction End Date: 4 Q 2019
