

BABCOCK ROAD PHASE V



Bexar County Public Works



PROJECT LOCATION





BABCOCK ROAD PHASE V

Overview




- ❑ Babcock Road Phase V begins just north of Heuermann Road and towards the south 1.4 miles to just south of Camp Bullis Road
 - Project will expand the current 2-lane roadway to include 2-12' lanes (one in each direction) with 4' shoulders.
 - Four bridges will be constructed to replace existing low-water crossings/low-lying areas.
 - Babcock Road will be raised in conjunction with the addition of the bridges to remove the roadway from the 100-year floodplain.
 - New driveway approaches.

- ❑ Construction Cost Estimate \$7.3 million




BABCOCK ROAD PHASE V

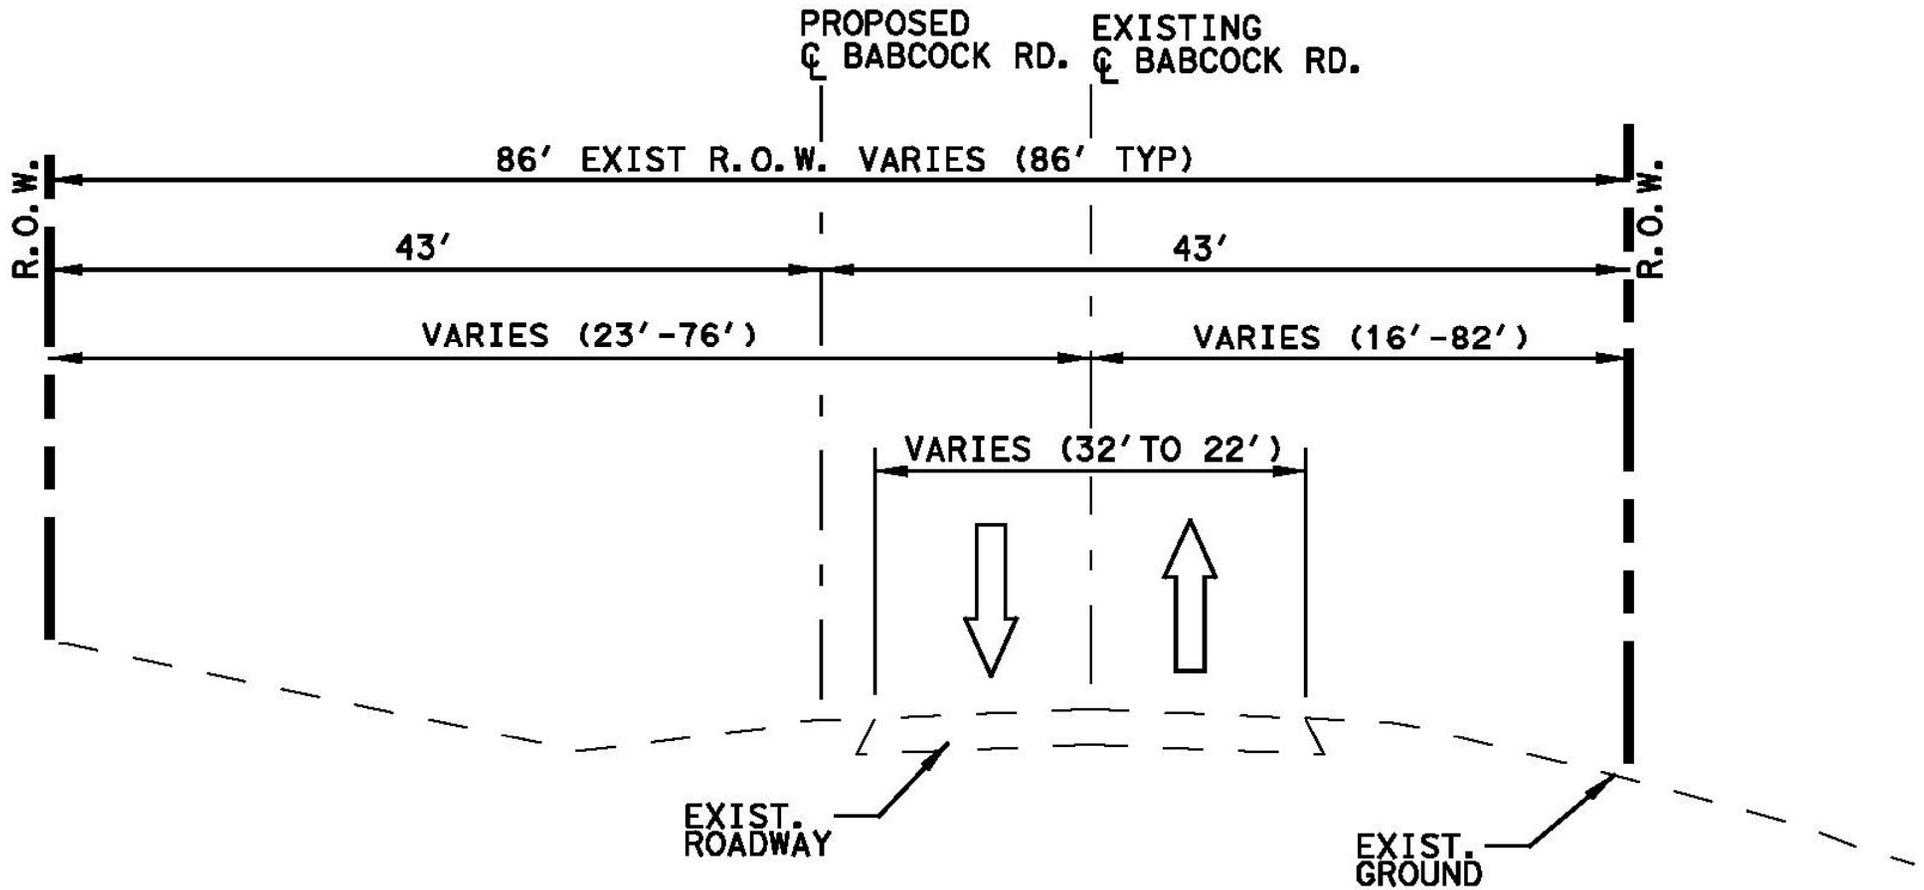

EXISTING ROADWAY TYPICAL SECTION



BABCOCK ROAD PHASE V

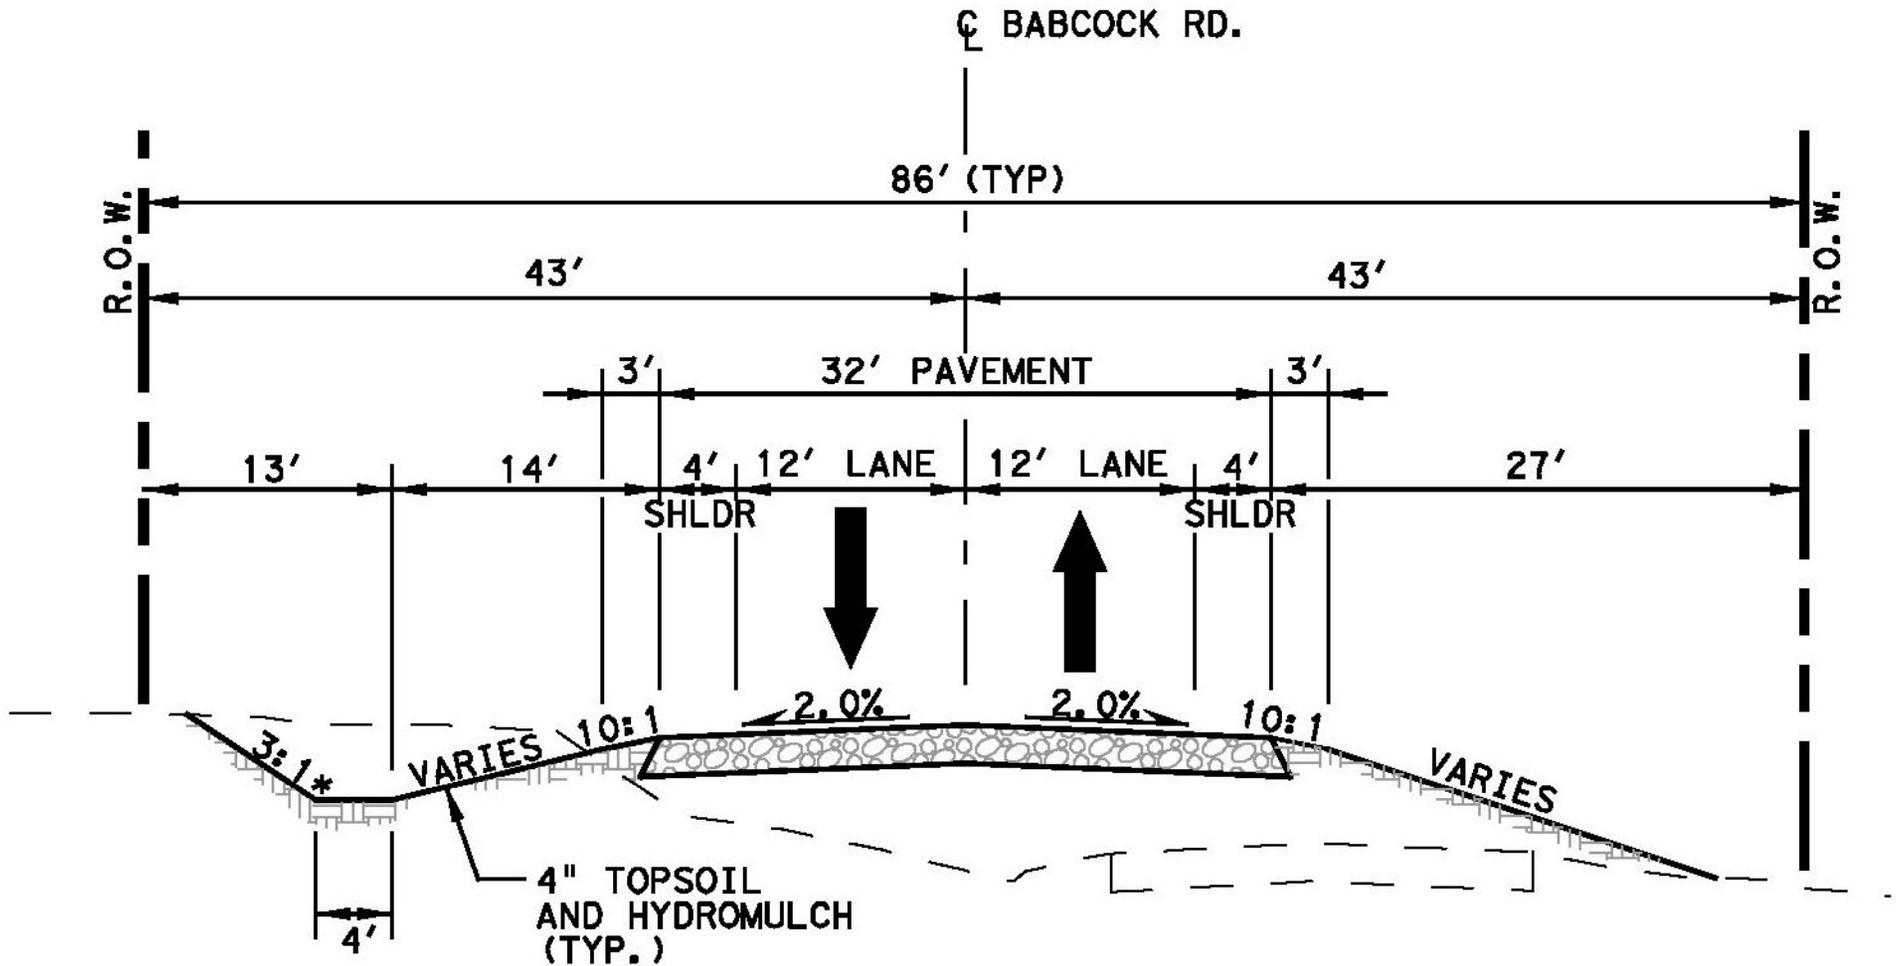

PROPOSED TYPICAL SECTION



BABCOCK ROAD PHASE V

Phase I Construction Sequence

- Construction will begin just north of Heuermann Road.
- Heuermann Road will be closed will the box culverts are constructed across Heuermann at Babcock Road.
- When this work is completed, Babcock Road will be closed to through traffic. Phase I Detour will be implemented. Heuermann Road, IH-10 and Camp Bullis Road will be used to detour traffic.
- Work will be from immediately north of Heuermann Road to just south of Luskey Blvd.
- Anticipated duration of this Phase will be 9-12 months



BABCOCK ROAD PHASE V

Phase II Construction Sequence

- Construction will begin just south of Luskey Blvd.
- Babcock Road will be closed from just south of Luskey to just south of the main entrance into The Estates of Cantera Apartments to through traffic
- Local access will be provided 24/7.
- Phase II & III Detour will be implemented. Luskey Blvd. and Camp Bullis Road will be used to detour traffic
- Anticipated duration of this Phase will be 6-9 months



BABCOCK ROAD PHASE V

Phase III Construction Sequence

- Construction will begin just south of main entrance into The Estates of Cantera Apartments.
- Babcock Road will be closed from just south of the main entrance into The Estates of Cantera Apartments to just north of Camp Bullis Road to through traffic
- Local access will be provided 24/7.
- Phase II & III Detour will be implemented. Luskey Blvd. and Camp Bullis Road will be used to detour traffic
- Anticipated duration of this Phase will be 9-12 months



BABCOCK ROAD PHASE V

Phase IV Construction Sequence

- Construction will begin just north of Camp Bullis Road to approximately 500 foot south of Camp Bullis Road.
- Two lanes, one each way, will be maintained on Babcock Road throughout this Phase of construction.
- Final overlay and permanent pavement strips for the entire project length will be completed during this Phase of work.
- Anticipated duration of this Phase will be 1-2 months



Contact Information

David R. Wegmann, P.E.
Engineering Services Manager – Transportation
233 N. Pecos La Trinidad, Suite 420
San Antonio, Texas 78207

Main: (210) 335-6700
Direct: (210) 335-3816

Email: dwegmann@bexar.org
